

Tates Creek Middle -- Renovation

- ▶ Architect: Ross Tarrant Architects
- ▶ General Contractor: D.W. Wilburn, Inc.
- ▶ Substantial Completion Date: October 2012
- ▶ GC Contract Sum: \$15,614,500
- ▶ Total Project Cost: \$18,854,244
- ▶ Change Orders to Date (5): \$253,051
- ▶ Current Phase: 4
- ▶ Estimated Completion: 79%



Tates Creek Middle -- Renovation

Rendering of Final Façade



December 2011

Tates Creek Middle -- Renovation

▶ **Work Completed to Date:**

- ▶ Gymnasium and locker rooms are substantially complete and the user has taken occupancy.
- ▶ Translucent skylights are installed above interior corridors.
- ▶ Installation of aluminum windows/storefront is nearly complete (caulking is in progress).
- ▶ Ceramic wall tile in the restrooms is complete.
- ▶ Ceramic tile backsplash at EWC's in corridors is complete.
- ▶ Daikin units are set.

Tates Creek Middle -- Renovation

▶ **Current Work Effort (December):**

- ▶ Metal roofing and wall panels above interior corridors are in progress.
- ▶ Interior hollow metal frames are installed and are being painted.
- ▶ CMU walls have been coated with block filler and accent walls are receiving the first coat of paint.
- ▶ Metal stud/Gypsum partitions are in progress.
- ▶ Installation of framing and gypsum for arched soffits in interior corridors is approximately 95% complete.

Tates Creek Middle -- Renovation


Gym Locker Rooms



Translucent Skylights



Interior Hollow Metal Frames

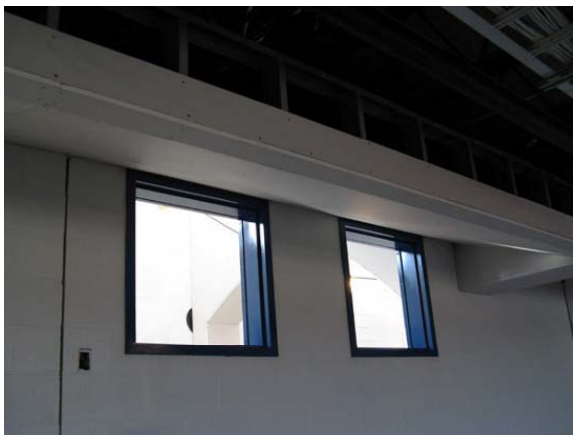

Ceramic Tile Walls in Restrooms




December 2011

Tates Creek Middle -- Renovation

Tile Backsplash in Corridors



Arched Soffits

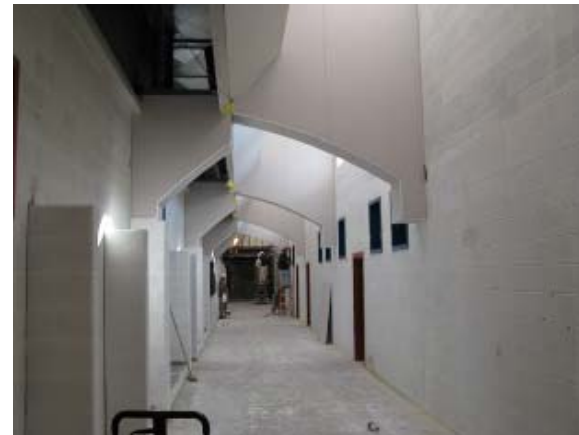

Daikin Units



Bleachers

