



Update on FCPS Construction/Renovation Projects

June 2018



New Elementary at Athens-Boonesboro

▶ Architect:	EOP Architects
▶ General Contractor:	Griggs Enterprises
▶ GC Contract Sum:	\$17,860,200
▶ Total Project Cost:	\$23,801,841
▶ Change Orders to Date (I):	\$58,598.34
▶ Scheduled Contract Completion Date:	July 2019
▶ % of Contract Completed:	7.39%
▶ Revised Completion Date per GC:	No Change

New Elementary at Athens-Boonesboro


Schematic Rendering of Final Façade



New Elementary at Athens-Boonesboro

▶ **Work Completed to Date:**


- ▶ Continue grading outside of building pad
- ▶ Began footers/foundation walls – Sector C
- ▶ Underground mechanical/electrical – Sector C & part of Sector D
- ▶ Began gravel install – Sector C
- ▶ Pour concrete in part of Sector C
- ▶ Began footers/foundation walls – Sector D/E
- ▶ Began installation of lift station and forced main

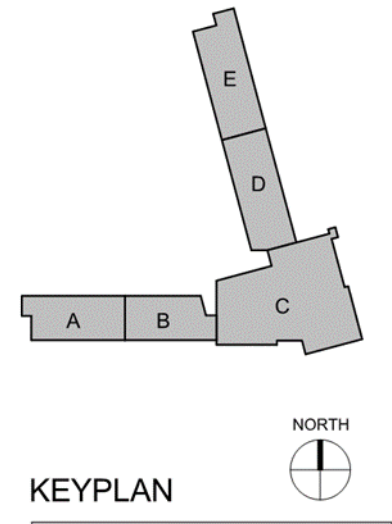

New Elementary at Athens-Boonesboro

▶ **Current Work Effort (June):**

- ▶ Continue grading outside of building pad
- ▶ Pour remaining concrete – Sector C
- ▶ Start masonry – Sector C
- ▶ Continue with forced main and lift station install
- ▶ Underground mechanical/electrical – Sectors D & E
- ▶ Start footer/foundation walls – Sectors A & B

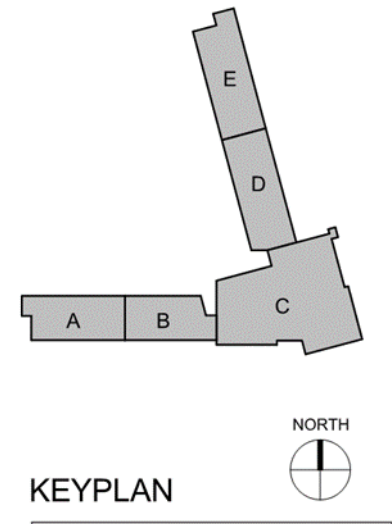

New Elementary at Athens-Boonesboro

Grading – Play Field Area



Gym



View Towards Front Door



Café & Gym Storage



New Elementary at Athens-Boonesboro

Interior Foundations



Looking North



Interior Foundations



Looking South

