


Lafayette High Stadium – Replacement

- ▶ Architect: Strand & Associates
- ▶ General Contractor: Judy Construction Co.
- ▶ Substantial Completion Date: October, 2010
- ▶ GC Contract Sum: \$4,333,000
- ▶ Total Project Cost: \$4,899,578
- ▶ Change Orders to Date (4): \$68,439
- ▶ Current Phase: Phase I
- ▶ Estimated Completion: 93%



Lafayette High Stadium – Replacement

New Football Stadium

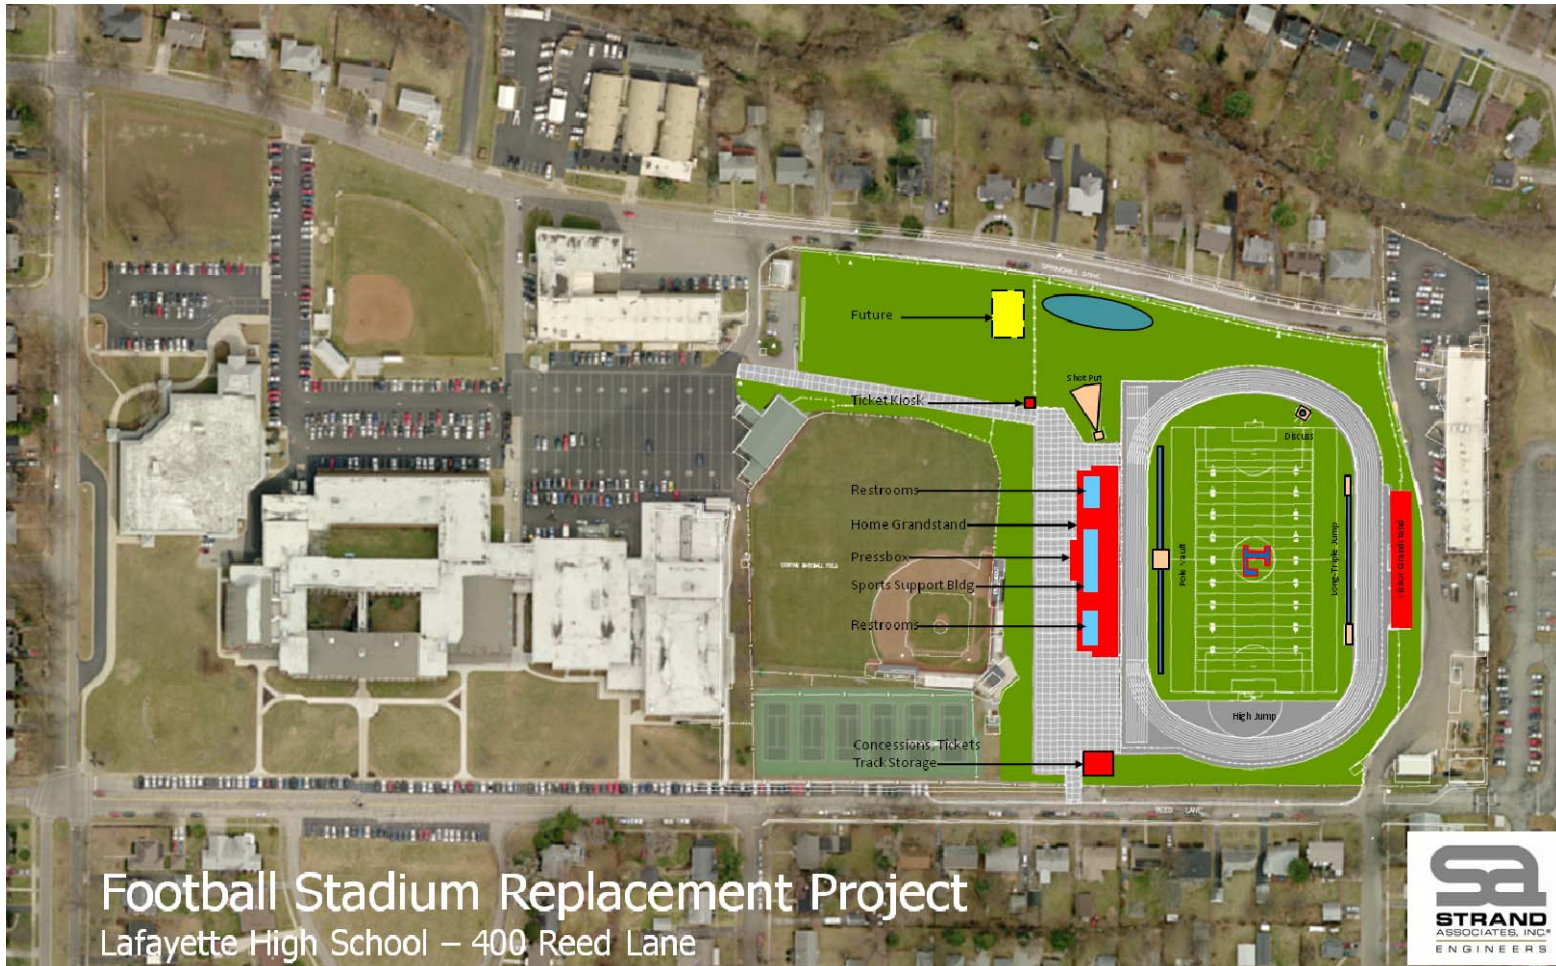

October 2010

Lafayette High Stadium – Replacement

▶ **Work Completed in Last 30 Days:**

- ▶ Site is substantially complete.
- ▶ Temporary Occupancy was granted.

▶ **Current Work Effort (October):**

- ▶ Touch up work will continue.
- ▶ Application of track surface is to be scheduled.
- ▶ Continue landscaping and final grading.



Lafayette High Stadium – Replacement

Football & Soccer Goals



Home Grandstands



Concession & Restroom Buildings



Inside Concession Building



Lafayette High Stadium – Replacement

Field from Home Grandstand



Back Side of Home Grandstand



Plaza & Home Grandstand



Inside Sport Support Building

